
ST22-3 2022 OVERLAY PROGRAM



CONSTRUCTION 80% | START DATE: 10/18/23 | COMPLETION DATE: 2/15/24

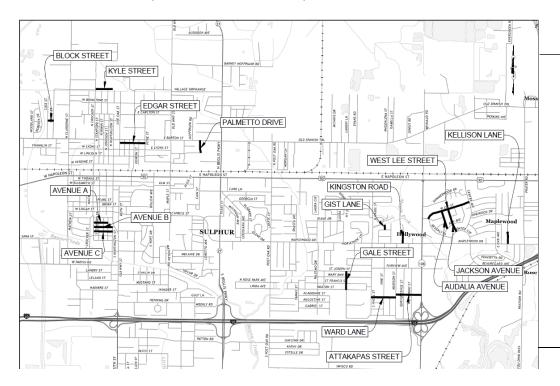

Engineer: Meyer & Associates Inc.

Bid Date: 8/8/2023

Notice of Award: 8/14/2023 Bid Award Amount: \$923,036.00

Contractor: R.C. Paving
Notice to Proceed: 10/18/2023
Est. Sub. Completion Date:

02/15/2024

SCOPE OF WORK

Project will consist of removal of existing roadway and repour of asphalt roadway.



