
ST19-1 MIMOSA HEIGHTS IMPROVEMENTS – PHASE 2



CONSTRUCTION 50% | START DATE: 6/13/22 | COMPLETION DATE: 11/10/22

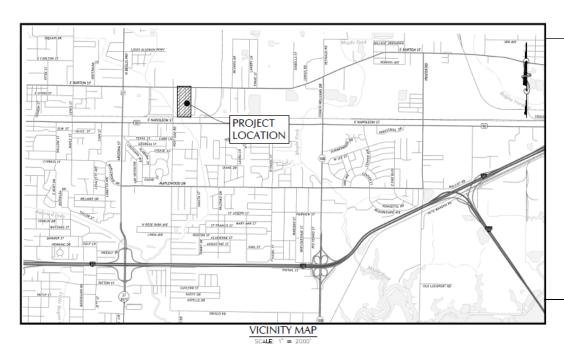

Engineer: Meyer & Associates Inc.

Bid Date: 2/10/22

Notice of Award: 2/14/22

Bid Award Amount: \$493,388.86 Contractor: Williams Equipment Services

Notice To Proceed: 6/13/22

Est. Sub. Completion Date: 11/10/22

SCOPE OF WORK

Project will consist of removal of existing roadway, reworking of subbase and repour of asphalt roadway.



