
WP22-3

NORTH WATER TREATMENT PROGRAM REMOVAL AND REPLACEMENT OF PRESSURE FILTERS



CONSTRUCTION 90% | START DATE: 12/4/2023 | COMPLETION DATE: 3/4/2025

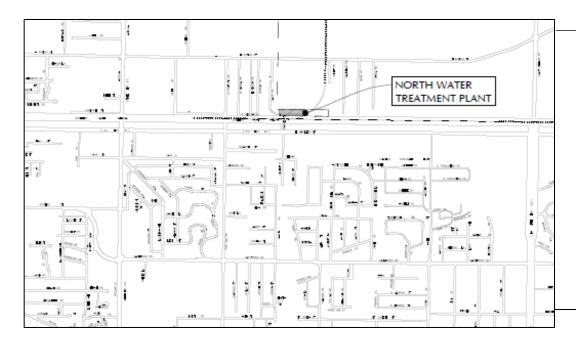

Engineer: Meyer & Associates Inc.

Bid Date: 3/28/2023

Notice of Award: 7/6/2023

Bid Award Amount: \$3,473,620.00 Contractor: The Lemoine Compnay, LLC

Notice To Proceed:12/4/2023

Est. Sub. Completion Date: 3/4/2025 Actual Completion Date: TBA

SCOPE OF WORK

Project will consist of the removal and replacement of the the pressure filters at the North Water Plant.



