



**SP22-1**

# WASTEWATER PLANT – SBR BASIN IMPROVEMENTS – PHASE 2



CONSTRUCTION 50% | START DATE: 11/1/2023 | COMPLETION DATE: 3/10/2025

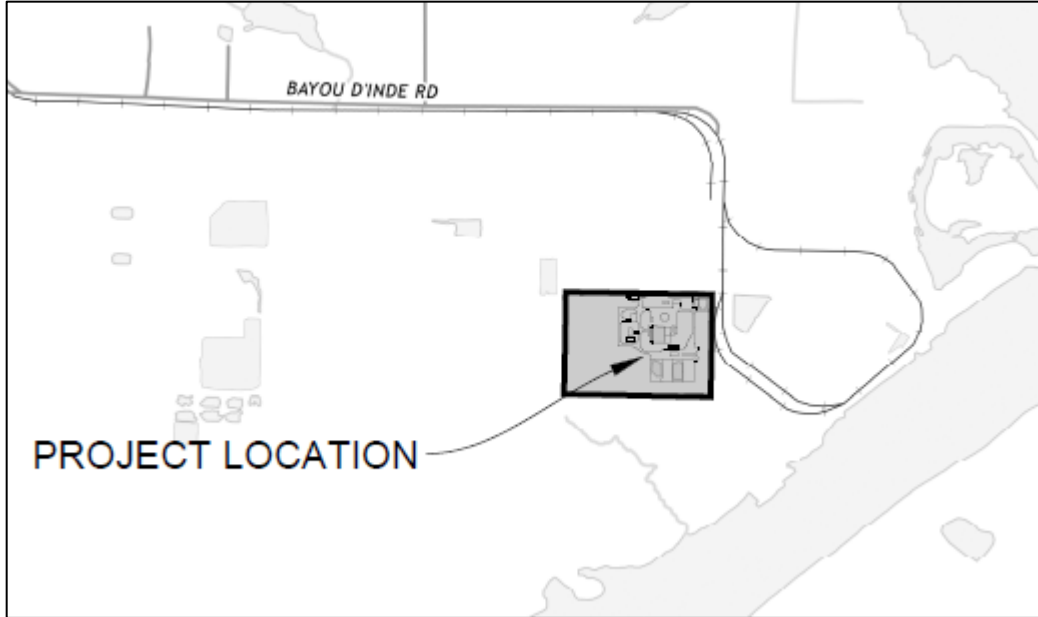

Engineer: Meyer & Associates Inc.  
Bid Date: 4/18/2023  
Notice of Award: 5/8/2023  
Bid Award Amount: \$6,996,000.00  
Contractor: Wharton-Smith, Inc.  
Notice To Proceed: 11/1/2023  
Est. Sub. Completion Date: 3/10/2025  
Actual Completion Date: TBA

## SCOPE OF WORK

Project will consist of removing and replacing all decantor control butterfly valves at the Sulphur Wastewater Plant Treatment Facility.

