



SP23-1 UV LIGHT SYSTEM FOR DISINFECTION



CONSTRUCTION 100% | START DATE: 7/1/2023 | COMPLETION DATE: 2/25/2024

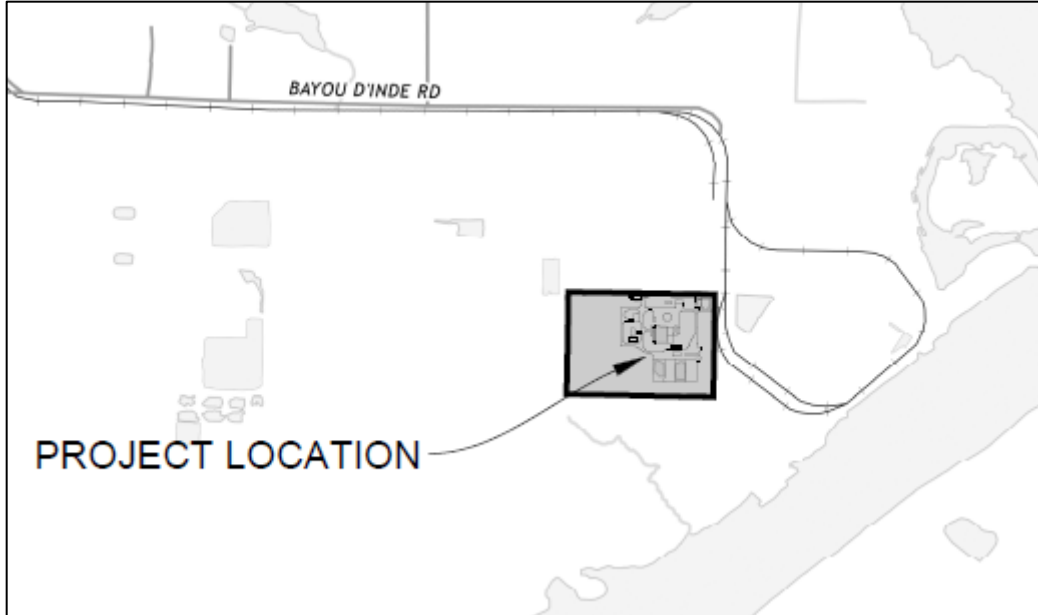

Engineer: Meyer & Associates Inc.
Bid Date: 7/8/22
Notice of Award: 7/11/22
Bid Award Amount: \$651,025.00
Contractor: Coastal Process, LLC
Notice To Proceed: 7/1/2023
Est. Sub. Completion Date:
2/25/2023

SCOPE OF WORK

The project will consist of new UV components and control systems within the existing ultraviolet disinfection system structure. Pictures show the existing system before upgrades will be done.

