



LS1912

HOUSING AUTHORITY SANITARY SEWER LIFT STATION IMPROVEMENTS



CONSTRUCTION 90% | START DATE: 6/5/2023 | COMPLETION DATE: 12/2/2023

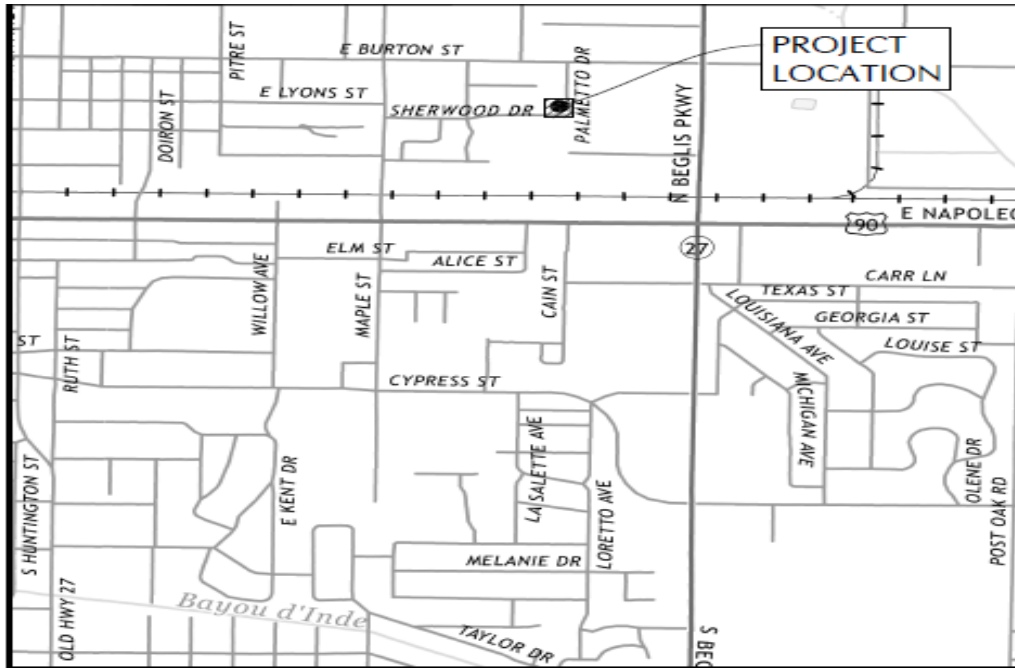

Engineer: Meyer & Associates Inc.
Bid Date: 8/8/2022
Notice of Award: 9/12/2022
Bid Award Amount: 625,457
Contractor: MPB Construction, LLC
Notice To Proceed: 6/5/2023
Est. Sub. Completion Date: 12/2/2023
Actual Completion Date: TBA

SCOPE OF WORK

The project will consist of relocation and reconstruction of new lift station.

