



CP19-1 DEMOLITION OF MUNICIPAL COMPLEX



CONSTRUCTION 10% | START DATE: 2/23/2026 | COMPLETION DATE: 5/24/2026

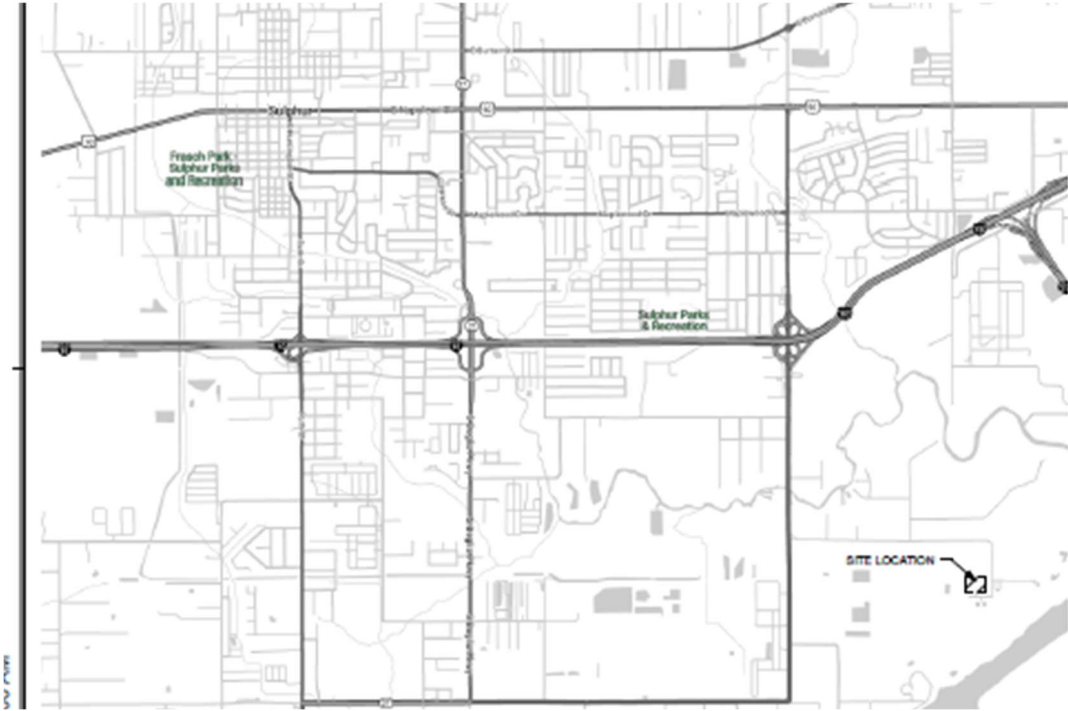

Engineer: Meyer & Associates Inc.
Bid Date: 11/20/2025
Notice of Award: 12/8/2025
Bid Award Amount: 725,000.00
Contractor: Pat Williams Construction, LLC
Notice To Proceed: 2/23/2026
Est. Sub. Completion Date: 5/24/2026

SCOPE OF WORK

This is for the demolition and abatement of the Sulphur Municipal Complex.

