



WP24-1

SULPHUR VERDINE WATER PLANT IMPROVEMENTS (PHASE 3)



CONSTRUCTION 50% | START DATE: 8/4/2025 | COMPLETION DATE: 9/3/2026

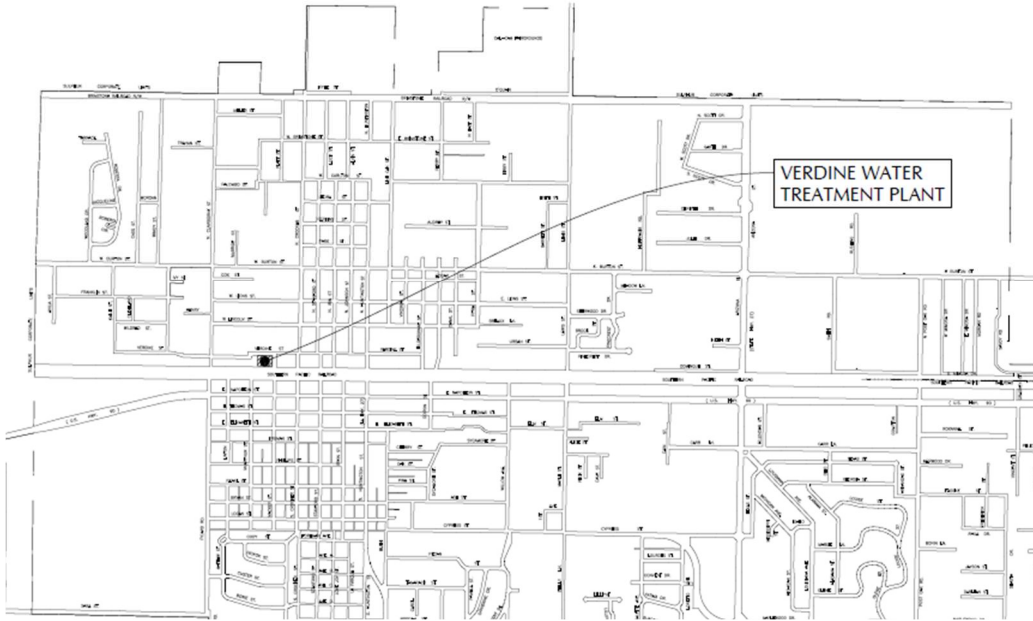

Engineer: Meyer & Associates Inc.
Cost Estimate: 5,605,750.00
Bid Date: 2/20/2025
Notice of Award: 3/10/2025
Bid Award Amount: \$6,418,000
Contractor: The Lemoine Company, LLC
Notice To Proceed: 8/4/2025
Est. Sub. Completion Date: 9/3/2026
Actual Completion Date: TBA

SCOPE OF WORK

This project will consist of a pre-treatment system including lamella clarifier, backwash system and associated piping at the Verdine Water Plant.

