



# SP22-9

# WWP EMERGENCY POWER GENERATOR AND ELECTRICAL SWITCHGEAR



CONSTRUCTION 60% | START DATE: 9/4/2024 | COMPLETION DATE: 4/21/2026

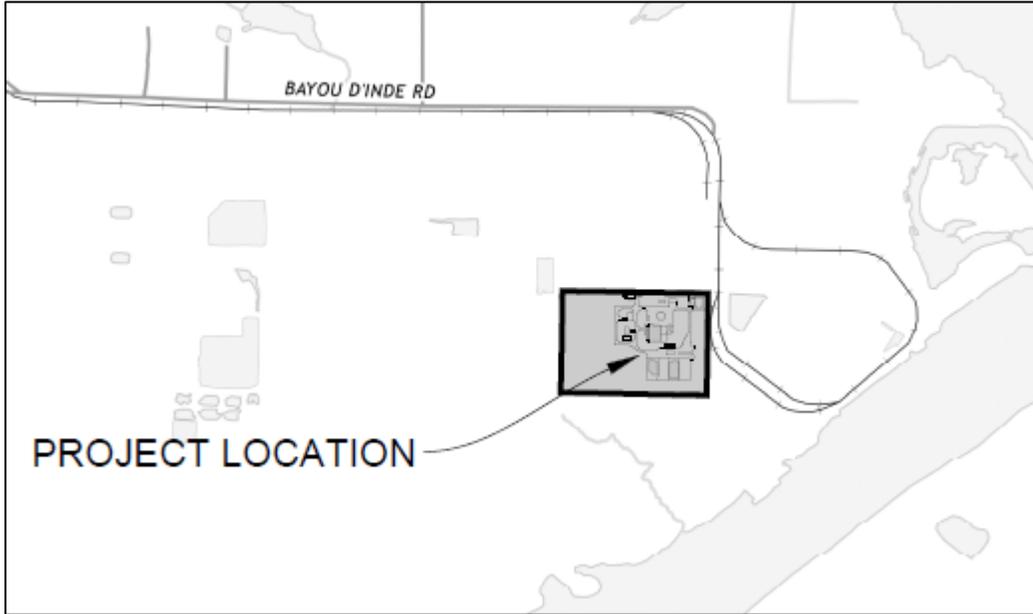

Engineer: Meyer & Associates Inc.  
Cost Estimate: 2,200,000  
Bid Date: 8/8/2024  
Notice of Award: 8/13/2024  
Bid Award Amount: 3,089,900.00  
Contractor: Kaough & Jones Electric Co, Inc.  
Notice To Proceed: 9/4/2024  
Est. Sub. Completion Date: 4/21/2026  
Actual Completion Date: TBA

## SCOPE OF WORK

The project will consist of replacement of existing damaged 2,500 kW generator with two 1,500 kW generators.

